



SUBMITTAL COVER SHEET

PROJECT NAME: ENCORE

Date: 6/12/2025

PROJECT LOCATION: 233 12th St S
Naple, FL 34102

GENERAL CONTRACTOR: BCBE

SUBMITTAL ITEM: SOG SAW CUTS


SPEC. SECTION: 03 30 00

Item	Description	Pgs
1	Cover Sheet	1
2	S202 - Ground Floor Framing Plan Rev.06	2
3	S203 - Ground Floor Framing Plan Rev.06	3
4		
5		
6		

Project Manager
Don Schallert

REMARKS: For review and approval

APPROVED STAMPS

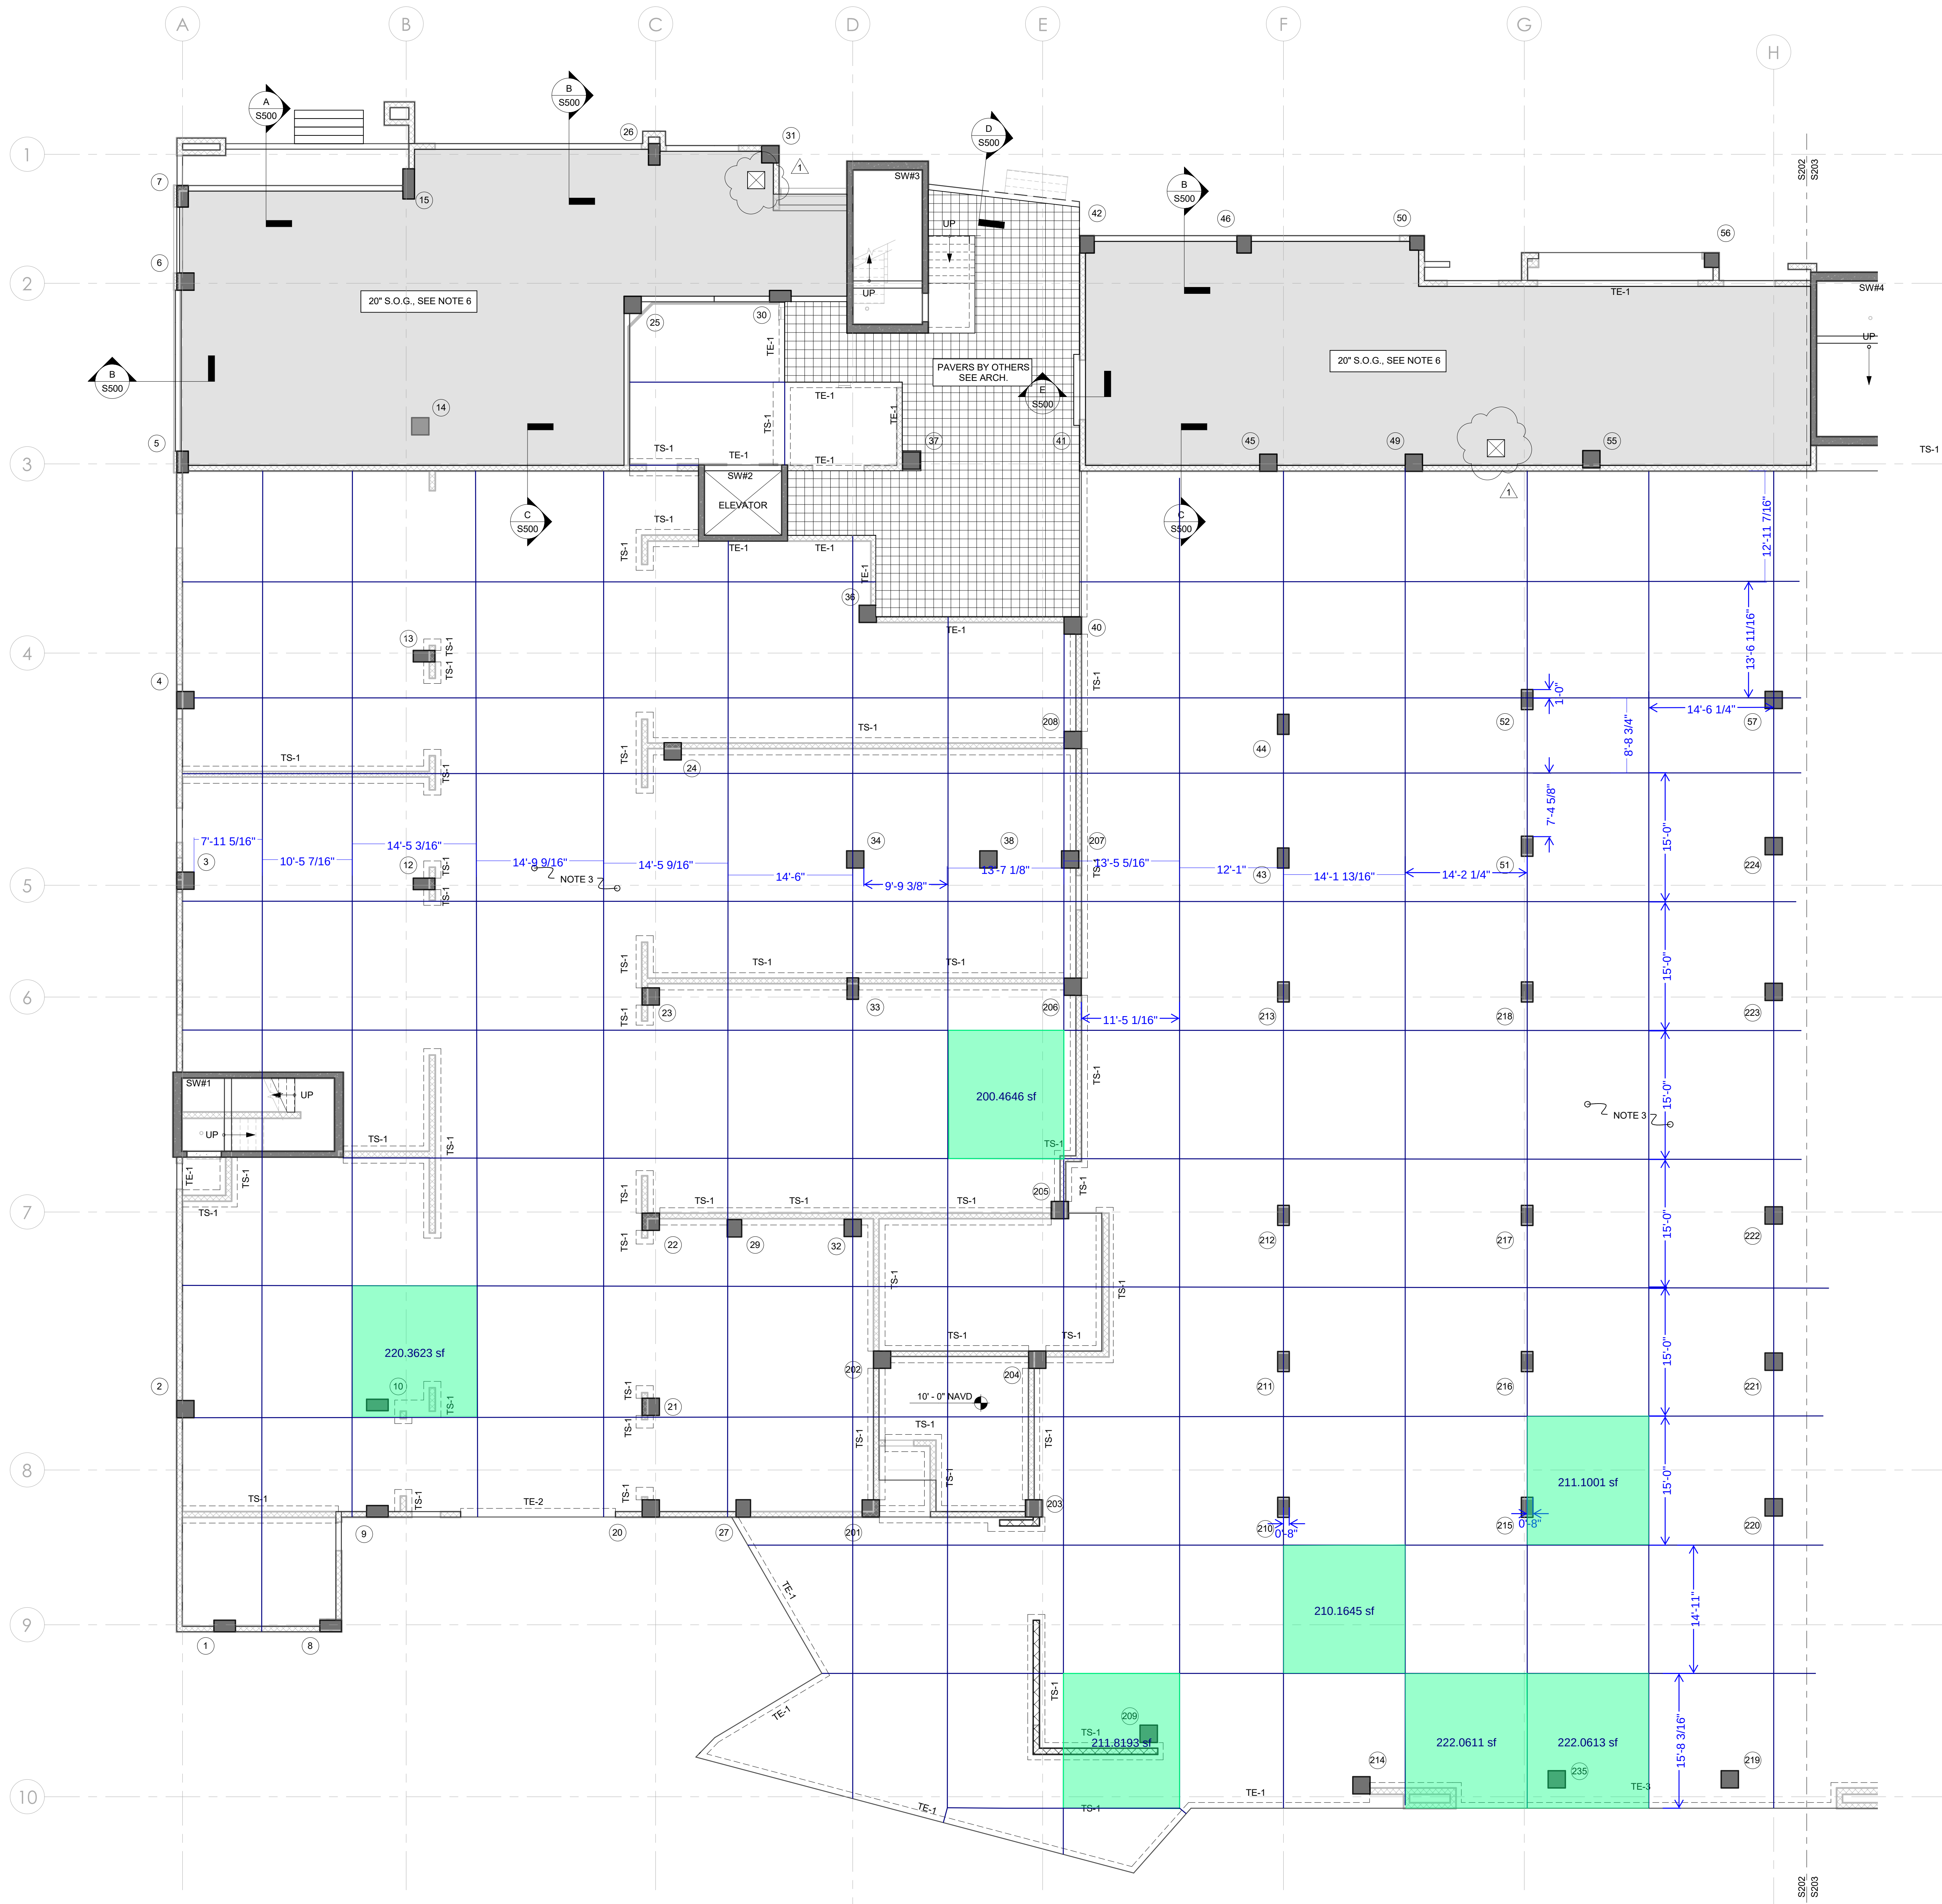

GROUND FLOOR FRAMING PLAN

SCALE: 1/8" = 1'-0"

- PLAN NOTES:**
- CONTRACTOR SHALL VERIFY LOCATION OF COLUMNS, WALLS AND EDGE OF SLABS WITH THE ARCHITECTURAL DRAWINGS. ANY DISCREPANCIES SHALL BE BROUGHT TO THE ATTENTION OF B&W STRUCTURAL DESIGNS, LLC. PRIOR TO PROCEEDING WITH THE AFFECTED PART OF WORK.
 - REFERENCE THE FOLLOWING SHEET SERIES FOR ADDITIONAL INFORMATION:
S100 SERIES: STRUCTURAL NOTES, TYPICAL SECTIONS & DETAILS.
S200 SERIES: FRAMING PLANS
S300 SERIES: COLUMN, SHEARWALL AND BEAM SCHEDULES AND DETAILS.
S400 SERIES: STAIR SECTIONS
S500 SERIES: MISC. SECTIONS AND DETAILS
 - SLAB ON GRADE TO BE 5" THICK U.N.O. WITH (1) LAYER OF 6X6-W2.9XW2.9 WELDED WIRE FABRIC (W.W.F.) CAST OVER WELL COMPACTED FILL. CONTRACTION JOINTS SHALL BE CUT OR TOOLED AND PERFORMED 4 TO 16 HOURS AFTER CONCRETE IS PLACED WITHOUT RAVELING CONCRETE SURFACE. JOINTS TO BE PLACED TO AN AREA APPROXIMATELY SQUARE AND LIMITED TO 225 SF.
 - INDICATES 8" INFILL NON-LOAD BEARING MASONRY WALLS EXTERIOR. WALLS TO BE REINFORCED WITH #7 VERTICALS AT SIDES OF OPENINGS GREATER THAN 2'-0", ENDS OF WALLS, INTERSECTIONS OF WALLS, CORNERS AND AT 32" O.C. MAX. (U.N.O.)
 - INDICATES 8" INFILL NON-LOAD BEARING MASONRY WALLS INTERIOR. WALLS TO BE REINFORCED WITH #5 VERTICALS AT SIDES OF OPENINGS GREATER THAN 2'-0", ENDS OF WALLS, INTERSECTIONS OF WALLS, CORNERS AND AT 72" O.C. MAX. (U.N.O.)
 - INDICATES 12" INFILL NON-LOAD BEARING MASONRY WALLS. WALLS TO BE REINFORCED WITH #7 VERTICALS AT SIDES OF OPENINGS GREATER THAN 2'-0", ENDS OF WALLS, INTERSECTIONS OF WALLS, CORNERS AND AT 40" O.C. MAX. (U.N.O.)
 - SEE ARCH. FOR FLOW-THRU VENTS & LOUVER LOCATIONS & SIZES.
 - FUTURE SLAB TO BE 20" THICK U.N.O. WITH 8/12 T/B E.W. OVER WELL COMPACTED FILL. SEE ARCH. FOR WATERPROOFING DETAILS.

COLUMN SYMBOLS

- INDICATES COLUMN BELOW
- INDICATES COLUMN THRU
- INDICATES COLUMN ABOVE

STEEL SYMBOLS

- BAR SIZE: 4 / 12 T
BAR SPACING: T=TOP, B=BOTTOM, C=C, E=E'
BAR PLACEMENT: T=TOP, B=BOTTOM, C=C, E=E'

THIS ITEM HAS BEEN ELECTRONICALLY SIGNED AND SEALED BY CHRISTOPHER S. WRIGHT, PE ON 03/27/2025 USING A DIGITAL SIGNATURE. PRINTED COPIES OF THIS DOCUMENT ARE NOT CONSIDERED SIGNED AND SEALED AND THE SIGNATURE MUST BE VERIFIED ON ANY ELECTRONIC COPIES.

b&w structural designs, llc.


105 S. Albany Avenue
Tampa, FL 33606 (813) 374-2459

www.structural-designs.com

CERTIFICATE OF AUTHORIZATION NUMBER: 8352

TO THE BEST OF MY KNOWLEDGE AND ABILITY, THE COMPLETED STRUCTURE DEPICTED ON THESE PLANS COMPLIES WITH THE APPLICABLE MINIMUM BUILDING CODES.

JOB NUMBER: 22-143

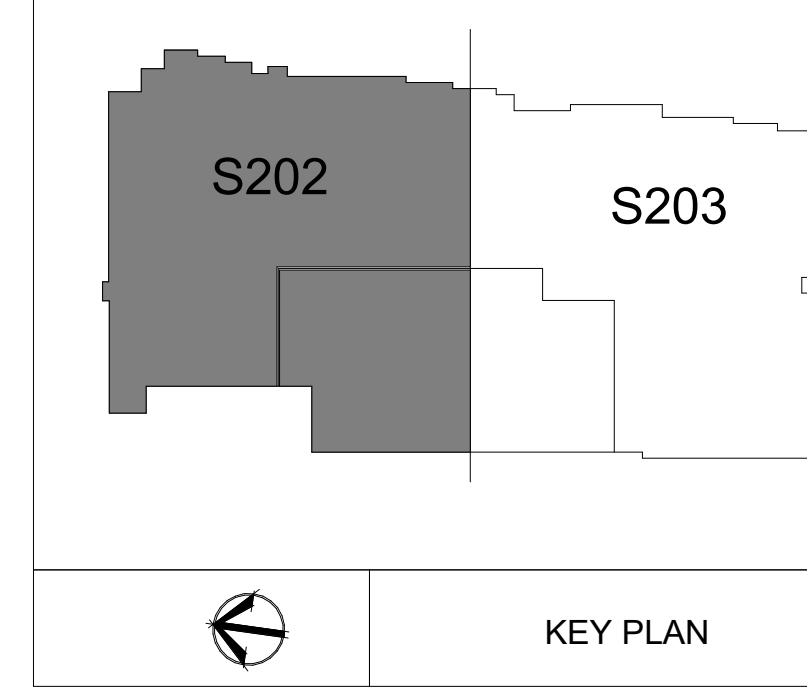


M-K
ARCHITECTURE
& PLANNING

816 SOUTH MAIN STREET
SUITE B
GREENVILLE, SC 29601
PHONE: (864)608-2324
WWW.MHKAP.COM

CONSULTANT:

NAPLES SQUARE NORTH
(ENCORE)
233 12TH STREET SOUTH
NAPLES, FL 34102




PERMIT SET	12/23/2024	Revision 1 - City Comments	02/20/25
------------	------------	----------------------------	----------

DRAWN BY: SS
CHECKED BY: CW

GROUND FLOOR FRAMING PLAN

PHASE PR NO PERMIT
22-143

S202

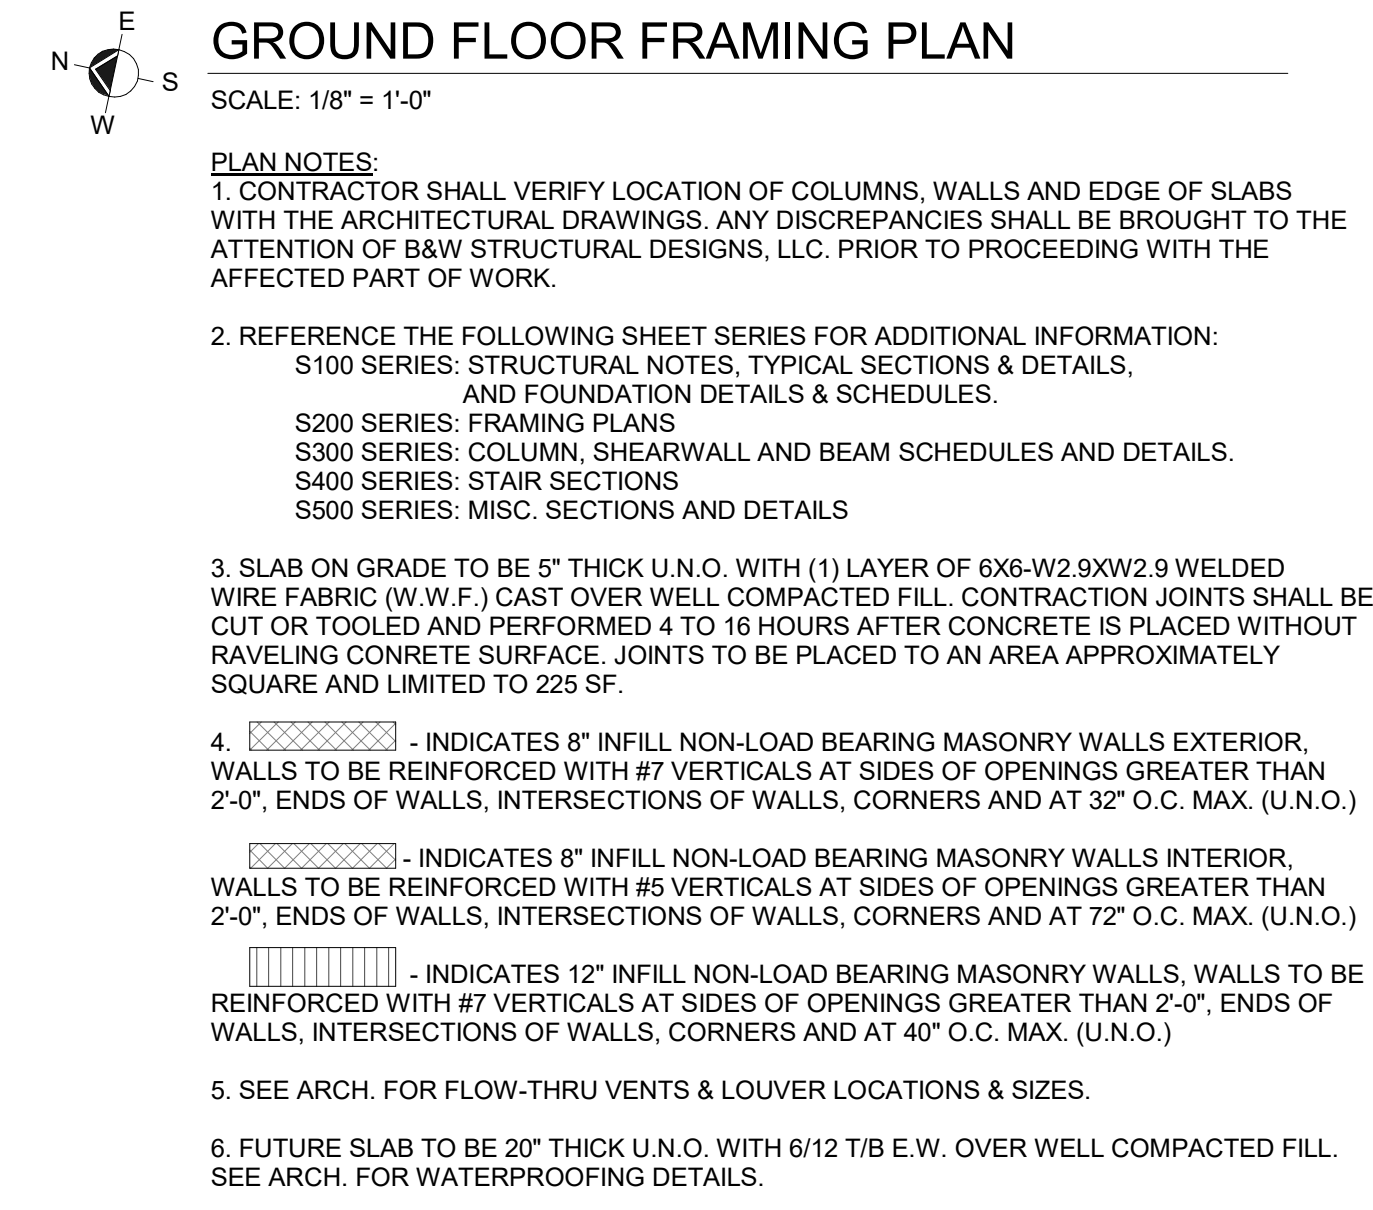

STEEL SYMBOLS

4 / 12 T

BAR SIZE
BAR SPACING
BAR PLACEMENT

T=TOP
B=BOTTOM
C='C'
E='E'

S203
